




INTERNAL CONSTRUCTION FEASIBILITY REVIEW

10/14/25

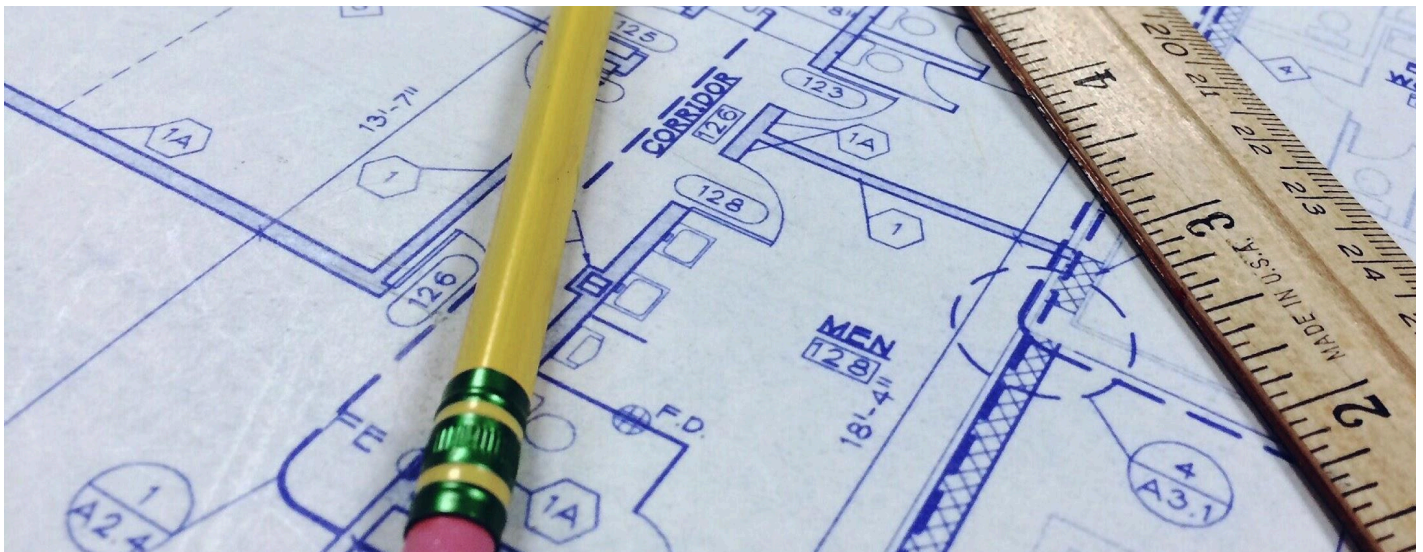

10910 Huston Street, North Hollywood, CA 91601

Sponsor:	AVENUE HOMES f/k/a THE RUN GROUP, LLC
Borrowing Entity:	10910 Huston LP
Approval status:	Approved
Report by:	Cynthia Moreno, Construction Underwriting

Executive Summary

Avenue Homes f/k/a The Run Group, LLC is overseen by Brandon Hance, who's collective real estate experience started in 2012. Real estate development is currently the core business for this Sponsor. Avenue Homes F/k/a The Run Group, LLC operates a 3rd party company as the general contractor, separating liabilities. At the moment, the Construction Underwriting Department has a draw hold for Subcontracts through Drywall with 0% of trades bought out. The cost spent on the file is mostly for soft costs.

This report is for the ED-1 Affordable Housing Project in North Hollywood, CA. Proposed construction for purposes of this review includes horizontal re-development of .19 acres and vertical construction of a 4-story multi-family building with 38 total units and 20,868 square feet of building area.

The Genesis Construction team has obtained a third-party feasibility, which has found overall cost to be reasonable. Therefore, the Genesis Capital Construction Department is in full support of funding this loan and feels that the Sponsor is proficient, knowledgeable and utilizing all appropriate resources to complete the project without issues.

The Genesis Capital Construction Department has received and reviewed a third-party feasibility from Trinity. The report concluded that the overall project risk rating is appropriate for the scope of work and meets best practice and is Recommended for Approval. The Genesis Capital Construction Department has reviewed all pertinent construction documents provided by the Sponsor and agrees with the third-party feasibility and has Approved the loan.

The overall project timeline is estimated to be 13 months with 13 months remaining and is deemed appropriate to substantially complete the subject project based on the Sponsor's track record and market standards.

For further analysis and additional information on the project, please see subsequent third-party review.

The Construction Department is draw holding for the following: Approved Plans, Approved Permits, Subcontractor Contracts

Loan Summary

Loan Type:	Ground-up Construction
Rehab Amount:	\$8,721,290.29
Construction Holdback:	\$7,964,285.12
Project Cost per Square Foot (GSF):	\$417.93
Project Cost per Structure:	\$8,721,290.29
Project Cost per Unit:	\$229,507.64
Total Contingency Included:	7.0%
Project Complete Percentage:	
Budget Determination:	The budget presented accurately reflects the scope of the project and the cost allocations have been determined to meet the minimum threshold to complete.
Additional Comments:	None
Plan Status:	Submittal/Plan Check (PC) - The plans received are sufficient to support the project scope as needed.
Permits Status:	The borrower has not yet obtained permits for this loan.

Permit Timeline:

Sponsor plans to have permits within 30 days after the funding of the loan.

Finished Product Details

Property Description:	Multifamily building in North Hollywood, CA
Number of Units:	38
Number of Stories:	Four-story
Gross Buildable SF:	20,868.00



Project Review

G25091023 - 10910 Huston
Street

PROJECT

10910 Huston Street
North Hollywood, CA 91601

Loan#: G25091023 - 10910 Huston
Street

LENDER

Genesis Capital

Ordered by: Construction UW

BORROWER

XXXXX-

BUILDER

This document may contain proprietary information. Please do not reveal any of its contents to anyone not directly responsible for evaluating it without first obtaining written permission from Trinity Inspection Services, LLC. © 2013 Trinity Inspection Services, LLC. Trademarks, Service marks, Copyrights are the property of TRINITY INSPECTION SERVICES, LLC. Business processes, technology or programming code may be protected under a U.S. Patent, Patent Pending or Registered Copyright. Additionally, this service is provided exclusively by Trinity Inspection Services, LLC and is EXCLUSIVELY responsible and liable for the scope of work to be completed, terms of the original contract, work flow processes, service levels, productivity measures, timelines, deliverables and all acts and/or omissions associated with this particular service.



1 Summary

Project Name	G25091023 - 10910 Huston Street
Project Address	10910 Huston Street North Hollywood CA 91601
Scope of Work	New Construction Project Review
Lender	Genesis Capital

Good afternoon, Underwriting Team!

I hope the Team is all well today!

I am pleased to present our report for the ED-1 Affordable Housing Project in North Hollywood, CA. Proposed construction for purposes of this review includes horizontal re-development of .19 acres and vertical construction of a 4-story multi-family building with 38 total units and 20,868 square feet of building area.

The Project Drawings provided for review include Architectural, Structural and Landscape Plans that are well detailed, dimensioned and enumerated further in this report. The Plans are mostly dated from the late 2024 thru mid-2025 with multiple revisions. The final revision is "Plan Check REV 02" set of plans. In my opinion, these plans are exceptional and wholly appropriate to construct the Project as proposed.

The Project Budget follows an extended mostly sequential format with line item detail for Horizontal and Vertical Costs that totals \$9,649,588.08. Allocated line item Costs include extensive Soft Costs that total \$2,782,408.54 with \$652,597.05 prepaid. Hard Costs total \$6,867,179.54 with all remaining. This Project Budget includes two Contingencies; one is a 'Scheduling' Contingency allocated \$180,979.17 with \$14,831.70 spent to date and the other is for \$323,923.56. Combined, the remaining Contingencies total \$490,071.03 that is a desirable 5.46% of the Total Remaining Budget.

The Line Item Analysis that follows shows that no line items appear HIGH or LOW compared to similarly scoped Projects. In addition, there are no 'Potential Added Costs' obvious in our analysis of the documents provided for review.

The primary metrics I track for comparable Multi-Unit Construction Projects are Cost per Square Foot and Cost per Unit. The metrics for the 10912 Huston build are \$462.41/Sq Ft and \$253,936.53/Unit. Both are achievable in the market compared to similarly scoped Projects.

In Summary, the Project Drawings are exceptional, the metrics are achievable and the Contingency is desirable. Therefore, this project as presented for Review is achievable with negligible risk to the Lender to fund as budgeted.

Upon review, if you or a member of your Team have any questions about this report, please let me know. Otherwise, we thank you for partnering with Trinity and wish you luck moving forward with this Project!

Kindest Regards,

Dave Taylor
VP-Commercial



2 Executive Summary

1 GEOTECHNICAL REPORT

No Soils Report was provided for Review.

2 PLANS AND CONTRACTS DOCUMENTS

CIVIL DRAWINGS

No Civil Drawings were provided for review.

LANDSCAPE DRAWINGS

Landscape Drawings prepared by Savage Land Design out of Fullerton, CA were provided for review.

Plans include Construction Layout Plans, Construction Details, Irrigation Notes & Calculations, Irrigation Hydrozones, Irrigation Layout Plan, Irrigation Details, Planting Layout Plan and Planting Details.

STRUCTURAL DRAWINGS

Structural Drawings prepared by IDG Structural Engineering out of Los Angeles, CA (Project # 202303) were provided for review.

Plans include Structural Notes, Concrete Details, Wood Framing Details, Shearwall Details, Strongwall Details, ATS Details, Masonry Details, Foundation Plan, Floor Framing Plans, Roof Framing Plan, Penthouse Framing Plan, Elevations, Foundation Details, Structural Framing Details, Elevator Details, Stair Details and Structural Steel Details.

ARCHITECTURAL DRAWINGS

Architectural Drawings prepared by Open Office out of Culver City, CA (Job # 202409) were provided for review.

Plans include General Sheets with Code Compliance, Exterior Wall Types, Interior Wall Types, Horizontal Assemblies, Fire Rating Notes & Details, Door and Window Types & Scheule, Typical Interior Door Details, a Slab Plan, Overall Floor Plans, Roof Plan, Reflected Ceiling Plans, Overall Finish Plan, Overall Exterior Elevations, Overall Building Sections, Enlarged Wall Sections, Window Details, Exterior Door Details, Cladding Details, Roof Details, Vertical Circulation, Stair, Handrail & Guardrail Details, Enlarged Unit Plans and Unit Bathroom Plans.

3 TRADE COMMENTS

No Electrical Drawings were provided for review.

No Mechanical Drawings were provided for review.

No Plumbing Drawings were provided for review.



4 ENVIRONMENTAL ASSESSMENTS

No Environmental Assessment was provided for Review.

5 CONSTRUCTION SCHEDULE

No Construction Schedule was provided for Review.

6 GENERAL CONTRACT

No General Construction Contract was provided for Review.

7 PROJECT BUDGET

Cumulative Project Bgt	\$9,649,588.08
Project Cost/SF	\$462.41
Project Cost/Unit	\$253,936.53

8 ACCESSIBILITY COMPLIANCE

Accessibility Compliance addressed on plan page G0.04 was provided for Review.

Details include Accessibility Notes & Info, Clearances, Reach/Mounting Heights, Accessibility Routes, Maneuvering Clearances, Grab Bars & Hand Rails, Lavatories & Sinks, Water Closet Plans, Roll-In Type Showers, Bathtub w/Moveable Seat, Elevator Clearances, Level Changes, Protruding Objects, Tactile Interior Signs and Water Closet Elevations.

9 CRITICAL ISSUES EFFECTING THE PROJECT

None.

10 DRAWING ENUMARATION

G0.00 06/13/25, G0.01 01/10/25, G0.03 11/26/24, G0.04 02/24/25, G0.05 02/24/25, G0.06 11/16/24, TOPO 07/23/24, G0.08 11/26/24, G0.09 07/07/25, G0.10 02/24/25, G0.11 06/13/25, G0.12 02/24/25, G0.13 12/04/24, G0.14 11/26/24, G0.15 11/26/24, G0.16 11/26/24, G0.17 06/13/25, G0.18 02/24/25, G0.20 02/24/25, G0.21 02/24/25, G0.22 02/24/25, G0.23 11/26/24, G0.30 NO DATE, G0.31 06/13/24, G0.32 06/13/25, G0.33 02/24/25, G0.34 02/24/25, G0.35 02/24/25, G0.40 06/13/25, G0.41 02/24/25, G0.42 11/26/24, G0.43 06/13/25, G0.44 06/13/25, G0.45 06/13/25, G0.46 06/13/25, G0.47 06/13/25, G0.50 02/24/25, G0.50.1 02/24/25, G0.51 02/24/25, G0.52 02/24/25, G0.52.1 02/24/25, G0.53 02/24/25, G0.53.1 02/24/25, G0.60 02/24/25, G0.61 02/24/25, G0.62 02/24/25, G0.63 02/24/25, G0.64 02/24/25, G0.65 02/24/25, G0.70 02/24/25, G0.71 06/13/25, G0.72 06/13/25, G0.73 NO DATE, G0.80 06/13/25, G0.81 06/13/25, G2.00 11/26/24, G-1.0 NO



DATE, G-2.0 NO DATE, RG-1.0 NO DATE, RG-2.0 NO DATE, CS 01/08/25, LC-1 01/08/25, LC-2 01/08/25, LI-1 01/08/25, LI-2 01/08/25, LI-3 01/08/25, LI-4 01/08/25, LI-5 01/08/25, LP-1 01/08/25, LP-2 01/08/25, A0.01 02/24/25, A0.03 02/24/25, A0.05 02/24/25, A0.10 02/24/25, A0.11 02/24/25, A0.12 02/24/25, A0.13 02/24/25, A0.15 02/24/25, A0.16 02/24/25, A0.17 02/24/25, A0.18 02/24/25, A0.20 02/24/25, A0.23 02/24/25, A1.01 02/24/25, A2.01 02/24/25, A2.02 02/24/25, A2.03 02/24/25, A2.04 02/24/25, A2.05 02/24/25, A2.07 11/26/24, A2.0711/26/24, A2.21 02/24/25, A2.22 11/26/24, A2.31 11/26/24, A2.32 11/26/24, A3.00 02/24/25, A3.01 02/24/25, A3.02 02/24/25, A4.00 02/24/25, A4.01 02/24/25, A4.10 02/24/25, A4.20 02/24/25, A4.21 02/24/25, A4.2211/26/24, A4.30 11/26/24, A4.31 11/26/24, A5.00 NO DATE, A5.10 11/26/24, A5.11 02/24/25, A5.12 02/24/25, A5.13 NO DATE, A5.20 NO DATE, A5.21 NO DATE, A5.22 NO DATE, A5.30 02/24/25, A5.31 NO DATE, A6.00 02/24/25, A6.01 02/24/25, A6.02 02/24/25, A6.03 02/24/25, A6.10 11/26/24, A6.11 02/24/25, A7.00 06/13/25, A7.01 06/13/25, A7.02 06/13/25, A7.03 06/13/25, A7.04 06/13/25, A7.05 06/13/25, A7.06 06/13/25, A7.07 02/24/25, A7.20 11/26/24, A7.30 02/24/25, A7.31 02/24/25, A7.32 11/26/24, A7.33 11/26/24, A7.60 11/26/24, A8.00 11/26/24, A9.01 NO DATE, S0.00 NO DATE, S0.01 NO DATE, S0.02 NO DATE, S0.03 NO DATE, S0.04 NO DATE, S0.05 NO DATE, S0.06 NO DATE, S0.07 NO DATE, S0.08 NO DATE, S0.09 NO DATE, S0.10 NO DATE, S0.11 NO DATE, S0.12 NO DATE, S0.13 NO DATE, S0.14 NO DATE, S2.01 NO DATE, S2.02 NO DATE, S2.02.1 NO DATE, S2.02.2 NO DATE, S2.03 NO DATE, S2.03.1 NO DATE, S2.03.2 NO DATE, S2.04 NO DATE, S2.04.1 NO DATE, S2.04.2 NO DATE, S2.05 NO DATE, S2.05.1 NO DATE, S2.05.2 NO DATE, S2.06 NO DATE, S3.00 NO DATE, S3.01 NO DATE, S3.02 NO DATE, S3.03 NO DATE, S6.00 NO DATE, S6.01 NO DATE, S6.02 NO DATE, S6.03 NO DATE, S6.04 NO DATE, S6.05 NO DATE.



3 Budgeted Cost

Order #	1553136
Report Completed	October 14, 2025
Gross Building Area	20,868

#	Description of Work	Budgeted Cost	Cost/SF (20,868)	Cost/Unit (38)	Opinion	Notes
1	Site Security	\$20,000.00	\$0.96	\$526.32	Estimate appears reasonable	Budgeted Cost is comparable to similarly scoped Projects. General Conditions vary by Contractor.
2	Soils Inspection	\$4,800.00	\$0.23	\$126.32	Estimate appears reasonable	Budgeted Cost is comparable to similarly scoped Projects. Consultant Costs vary by Project.
3	Offsites (Transformer)	\$20,000.00	\$0.96	\$526.32	Estimate appears reasonable	Budgeted Cost is comparable to similarly scoped Projects. Consultant Costs vary by Project.
4	Plan Check Fees	\$15,000.00	\$0.72	\$394.74	Estimate appears reasonable	Budgeted Cost is comparable to similarly scoped Projects. Consultant Costs vary by Project.
5	Permits	\$121,785.82	\$5.84	\$3,204.89	Estimate appears reasonable	Budgeted Cost is comparable to similarly scoped Projects. Municipal Fees vary by Location.
6	Survey	\$3,805.23	\$0.18	\$100.14	Estimate appears reasonable	Budgeted Cost is comparable to similarly scoped Projects. Consultant Costs vary by Project.
7	Soils Engineer	\$6,800.00	\$0.33	\$178.95	Estimate appears reasonable	Budgeted Cost is comparable to similarly scoped Projects. Consultant Costs vary by Project.
8	Soils Permit + T24	\$2,500.00	\$0.12	\$65.79	Estimate appears reasonable	Budgeted Cost is comparable to similarly scoped Projects. Municipal Fees vary by Location.
9	Special Inspections - Deputy	\$15,000.00	\$0.72	\$394.74	Estimate appears reasonable	Budgeted Cost is comparable to similarly scoped Projects. Consultant Costs vary by Project.



#	Description of Work	Budgeted Cost	Cost/SF (20,868)	Cost/Unit (38)	Opinion	Notes
10	Architect	\$113,100.00	\$5.42	\$2,976.32	Estimate appears reasonable	Budgeted Cost is comparable to similarly scoped Projects. Consultant Costs vary by Project.
11	Structural Engineer	\$31,600.00	\$1.51	\$831.58	Estimate appears reasonable	Budgeted Cost is comparable to similarly scoped Projects. Consultant Costs vary by Project.
12	Structural Observation	\$8,000.00	\$0.38	\$210.53	Estimate appears reasonable	Budgeted Cost is comparable to similarly scoped Projects. Consultant Costs vary by Project.
13	Civil Engineering	\$20,000.00	\$0.96	\$526.32	Estimate appears reasonable	Budgeted Cost is comparable to similarly scoped Projects. Consultant Costs vary by Project.
14	Grading Permit	\$2,313.40	\$0.11	\$60.88	Estimate appears reasonable	Budgeted Cost is comparable to similarly scoped Projects. Municipal Fees vary by Location.
15	Landscape Architect / Designer	\$4,200.00	\$0.20	\$110.53	Estimate appears reasonable	Budgeted Cost is comparable to similarly scoped Projects. Consultant Costs vary by Project.
16	Driveway Apron Permit	\$2,500.00	\$0.12	\$65.79	Estimate appears reasonable	Budgeted Cost is comparable to similarly scoped Projects. Municipal Fees vary by Location.
17	Punch List - Misc.	\$21,983.00	\$1.05	\$578.50	Estimate appears reasonable	Budgeted Cost is comparable to similarly scoped Projects. General Conditions vary by Contractor.
18	EBM, Low Voltage, Landscape, Waterproofing Ca	\$23,320.08	\$1.12	\$613.69	Estimate appears reasonable	Budgeted Cost is comparable to similarly scoped Projects. Consultant Costs vary by Project.
19	Project Accounting / Tax Filing	\$20,000.00	\$0.96	\$526.32	Estimate appears reasonable	Budgeted Cost is comparable to similarly scoped Projects. Soft Costs vary by Project.
20	Legal Expenses	\$10,000.00	\$0.48	\$263.16	Estimate appears reasonable	Budgeted Cost is comparable to similarly scoped Projects. Soft Costs vary by Project.
21	Sewer CCTV And Inspection	\$325.00	\$0.02	\$8.55	Estimate appears reasonable	Budgeted Cost is comparable to similarly scoped Projects. Consultant Costs vary by



#	Description of Work	Budgeted Cost	Cost/SF (20,868)	Cost/Unit (38)	Opinion	Notes
21	Sewer CCTV And Inspection	\$325.00	\$0.02	\$8.55	Estimate appears reasonable	Project.
22	Environmental Phase I	\$3,000.00	\$0.14	\$78.95	Estimate appears reasonable	Budgeted Cost is comparable to similarly scoped Projects. Consultant Costs vary by Project.
23	Dry Utility Consultant	\$17,000.00	\$0.81	\$447.37	Estimate appears reasonable	Budgeted Cost is comparable to similarly scoped Projects. Consultant Costs vary by Project.
24	Dry Utility Survey	\$5,000.00	\$0.24	\$131.58	Estimate appears reasonable	Budgeted Cost is comparable to similarly scoped Projects. Consultant Costs vary by Project.
25	MEP	\$46,400.00	\$2.22	\$1,221.05	Estimate appears reasonable	Budgeted Cost is comparable to similarly scoped Projects. Consultant Costs vary by Project.
26	Civil Construction Administration	\$5,000.00	\$0.24	\$131.58	Estimate appears reasonable	Budgeted Cost is comparable to similarly scoped Projects. Consultant Costs vary by Project.
27	Permit Clearances & Agency Reviews	\$40,000.00	\$1.92	\$1,052.63	Estimate appears reasonable	Budgeted Cost is comparable to similarly scoped Projects. Consultant Costs vary by Project.
28	Demo Permit Fees	\$500.00	\$0.02	\$13.16	Estimate appears reasonable	Budgeted Cost is comparable to similarly scoped Projects. Municipal Fees vary by Location.
29	MEP Fees	\$4,600.00	\$0.22	\$121.05	Estimate appears reasonable	Budgeted Cost is comparable to similarly scoped Projects. Municipal Fees vary by Location.
30	Agency Signoffs	\$7,000.00	\$0.34	\$184.21	Estimate appears reasonable	Budgeted Cost is comparable to similarly scoped Projects. Municipal Fees vary by Location.
31	Specifications Writer Consultant	\$2,000.00	\$0.10	\$52.63	Estimate appears reasonable	Budgeted Cost is comparable to similarly scoped Projects. Consultant Costs vary by Project.
32	Construction Consultant	\$3,500.00	\$0.17	\$92.11	Estimate appears reasonable	Budgeted Cost is comparable to similarly scoped Projects. Consultant Costs vary by Project.



#	Description of Work	Budgeted Cost	Cost/SF (20,868)	Cost/Unit (38)	Opinion	Notes
33	Low Voltage Consultant	\$15,000.00	\$0.72	\$394.74	Estimate appears reasonable	Budgeted Cost is comparable to similarly scoped Projects. Consultant Costs vary by Project.
34	Photovoltaic Consultant	\$5,000.00	\$0.24	\$131.58	Estimate appears reasonable	Budgeted Cost is comparable to similarly scoped Projects. Consultant Costs vary by Project.
35	Construction Management / Observation (Oo)	\$55,000.00	\$2.64	\$1,447.37	Estimate appears reasonable	Budgeted Cost is comparable to similarly scoped Projects. Consultant Costs vary by Project.
36	Soft Cost Contingency	\$32,919.95	\$1.58	\$866.31	Estimate appears reasonable	Budgeted Cost is 7.84% of Remaining Soft Costs.
37	CMFA Startup Fee	\$22,800.00	\$1.09	\$600.00	Estimate appears reasonable	Budgeted Cost is comparable to similarly scoped Projects. Municipal Fees vary by Location.
38	Non-Profit Start Up Fee	\$25,000.00	\$1.20	\$657.89	Estimate appears reasonable	Budgeted Cost is comparable to similarly scoped Projects. Municipal Fees vary by Location.
39	CMFA Construction Fee	\$12,000.00	\$0.58	\$315.79	Estimate appears reasonable	Budgeted Cost is comparable to similarly scoped Projects. Municipal Fees vary by Location.
40	Non-Profit Construction Fee	\$10,000.00	\$0.48	\$263.16	Estimate appears reasonable	Budgeted Cost is comparable to similarly scoped Projects. Municipal Fees vary by Location.
41	WTE Legal Costs For CMFA & Non-Profit Partner	\$20,000.00	\$0.96	\$526.32	Estimate appears reasonable	Budgeted Cost is comparable to similarly scoped Projects. Municipal Fees vary by Location.
42	Schedule Contingency	\$180,979.17	\$8.67	\$4,762.61	Estimate appears reasonable	Budgeted Cost is 39.62% of Remaining Soft Costs.
43	General Conditions	\$565,545.00	\$27.10	\$14,882.76	Estimate appears reasonable	Budgeted Cost is comparable to similarly scoped Projects. General Conditions vary by Contractor.
44	General Requirement	\$135,922.00	\$6.51	\$3,576.89	Estimate appears reasonable	Budgeted Cost is comparable to similarly scoped Projects. General Requirements vary by Contractor.



#	Description of Work	Budgeted Cost	Cost/SF (20,868)	Cost/Unit (38)	Opinion	Notes
45	Site Work	\$139,049.51	\$6.66	\$3,659.20	Estimate appears reasonable	Budgeted Cost/Unit is comparable to similarly scoped Projects.
46	Concrete	\$253,182.00	\$12.13	\$6,662.68	Estimate appears reasonable	Budgeted Cost/Unit is comparable to similarly scoped Projects.
47	Masonry	\$3,562.64	\$0.17	\$93.75	Estimate appears reasonable	Budgeted Cost/Unit is comparable to similarly scoped Projects.
48	Metals	\$324,100.00	\$15.53	\$8,528.95	Estimate appears reasonable	Budgeted Cost/Unit is comparable to similarly scoped Projects.
49	Framing	\$818,554.00	\$39.23	\$21,540.89	Estimate appears reasonable	Budgeted Cost/Sq Ft is comparable to similarly scoped Projects.
50	Countertops	\$56,930.00	\$2.73	\$1,498.16	Estimate appears reasonable	Budgeted Cost/Unit is comparable to similarly scoped Projects. No Specifications provided for Review.
51	Cabinets	\$56,930.00	\$2.73	\$1,498.16	Estimate appears reasonable	Budgeted Cost/Unit is comparable to similarly scoped Projects. No Specifications provided for Review.
52	Thermal Moisture Protection	\$173,148.00	\$8.30	\$4,556.53	Estimate appears reasonable	Budgeted Cost/Unit is comparable to similarly scoped Projects.
53	Doors	\$204,087.33	\$9.78	\$5,370.72	Estimate appears reasonable	Budgeted Cost/Unit is comparable to similarly scoped Projects. No Specifications provided for Review.
54	Windows	\$106,274.25	\$5.09	\$2,796.69	Estimate appears reasonable	Budgeted Cost/Unit is comparable to similarly scoped Projects. No Specifications provided for Review.
55	Stucco	\$208,002.00	\$9.97	\$5,473.74	Estimate appears reasonable	Budgeted Cost/Unit is comparable to similarly scoped Projects.
56	Drywall	\$416,355.00	\$19.95	\$10,956.71	Estimate appears reasonable	Budgeted Cost/Unit is comparable to similarly scoped Projects.



#	Description of Work	Budgeted Cost	Cost/SF (20,868)	Cost/Unit (38)	Opinion	Notes
57	Painting	\$120,700.00	\$5.78	\$3,176.32	Estimate appears reasonable	Budgeted Cost/Sq Ft is comparable to similarly scoped Projects.
58	Flooring - Common Areas	\$45,150.00	\$2.16	\$1,188.16	Estimate appears reasonable	Budgeted Cost/Unit is comparable to similarly scoped Projects. No Specifications provided for Review.
59	Flooring - Units With Baseboards	\$93,335.00	\$4.47	\$2,456.18	Estimate appears reasonable	Budgeted Cost/Unit is comparable to similarly scoped Projects. No Specifications provided for Review.
60	Specialties	\$25,109.21	\$1.20	\$660.77	Estimate appears reasonable	Budgeted Cost/Unit is comparable to similarly scoped Projects. No Specifications provided for Review.
61	Equipment	\$153,636.00	\$7.36	\$4,043.05	Estimate appears reasonable	Budgeted Cost/Unit is comparable to similarly scoped Projects. No Specifications provided for Review.
62	Fire Sprinklers	\$108,500.00	\$5.20	\$2,855.26	Estimate appears reasonable	Budgeted Cost/Unit is comparable to similarly scoped Projects.
63	Fire Alarm	\$68,401.00	\$3.28	\$1,800.03	Estimate appears reasonable	Budgeted Cost/Unit is comparable to similarly scoped Projects. No Specifications provided for Review.
64	Solar Panels	\$97,000.00	\$4.65	\$2,552.63	Estimate appears reasonable	Budgeted Cost/Unit is comparable to similarly scoped Projects. No Specifications provided for Review.
65	Security Access & Surveillance	\$136,430.00	\$6.54	\$3,590.26	Estimate appears reasonable	Budgeted Cost/Unit is comparable to similarly scoped Projects. No Specifications provided for Review.
66	Elevators & Lift	\$174,882.00	\$8.38	\$4,602.16	Estimate appears reasonable	Budgeted Cost/Unit is comparable to similarly scoped Projects. No Specifications provided for Review.



#	Description of Work	Budgeted Cost	Cost/SF (20,868)	Cost/Unit (38)	Opinion	Notes
67	Water Submeter (Material)	\$12,273.00	\$0.59	\$322.97	Estimate appears reasonable	Budgeted Cost is comparable to similarly scoped Projects. Consultant Costs vary by Project.
68	Rough Plumbing	\$751,927.00	\$36.03	\$19,787.55	Estimate appears reasonable	Budgeted Cost/Unit is comparable to similarly scoped Projects. No Plumbing Plans, Schedules or Details provided for Review.
69	Finish Plumbing	\$90,000.00	\$4.31	\$2,368.42	Estimate appears reasonable	Budgeted Cost/Unit is comparable to similarly scoped Projects. No Plumbing Plans, Schedules or Details provided for Review.
70	HVAC	\$259,000.00	\$12.41	\$6,815.79	Estimate appears reasonable	Budgeted Cost/Unit is comparable to similarly scoped Projects. No Mechanical or HVAC Plans, Schedules or Details provided for Review.
71	Electrical	\$880,486.32	\$42.19	\$23,170.69	Estimate appears reasonable	Budgeted Cost/Unit is comparable to similarly scoped Projects. No Electrical Plans, Schedules or Details provided for Review.
72	Contingency	\$323,923.56	\$15.52	\$8,524.30	Estimate appears reasonable	Budgeted Cost is 4.72% of Sub Total Hard Costs.
73	Insurance (GL w/ Auto, Workers Compl)	\$97,177.07	\$4.66	\$2,557.29	Estimate appears reasonable	Budgeted Cost is comparable to similarly scoped Projects. Soft Costs vary by Project.
74	Gross Receipt Tax	\$6,543.26	\$0.31	\$172.19	Estimate appears reasonable	Budgeted Cost is comparable to similarly scoped Projects. Municipal Fees vary by Location.
75	GC Fee	\$388,708.28	\$18.63	\$10,229.17	Estimate appears reasonable	Budgeted Cost is 5.66% of Sub Total Hard Costs.
76	Development Fee	\$335,434.00	\$16.07	\$8,827.21	Estimate appears reasonable	Budgeted Cost is comparable to similarly scoped Projects. Consultant Costs vary by Project.
77	Carrying Costs	\$122,215.00	\$5.86	\$3,216.18	Estimate appears reasonable	Budgeted Cost is comparable to similarly scoped Projects. Transaction Costs vary by Lender.
78	Financing Costs	\$917,384.00	\$43.96	\$24,141.68	Estimate appears reasonable	Budgeted Cost is comparable



#	Description of Work	Budgeted Cost	Cost/SF (20,868)	Cost/Unit (38)	Opinion	Notes
78	Financing Costs	\$917,384.00	\$43.96	\$24,141.68	Estimate appears reasonable	to similarly scoped Projects. Transaction Costs vary by Lender.
79		\$0.00	\$0.00	\$0.00		
80		\$0.00	\$0.00	\$0.00		
81		\$0.00	\$0.00	\$0.00		
82		\$0.00	\$0.00	\$0.00		
83		\$0.00	\$0.00	\$0.00		
TOTAL PROJECT BUDGET		\$9,649,588.08	\$462.41	\$253,936.53		

4 Potential Added Costs

POTENTIAL ADDED COSTS

None.

Total Budget Review is an analysis based on the Cost Breakdown, Landscaping, Structural and Architectural plans as enumerated. Any plans not specifically enumerated, municipal or owner changes and any other owner or developer requirements are not included.
